
GEOLAB & ENGINEERING KENYA LIMITED
Independent Materials Testing & Inspection Laboratories
Email : geolabengineeringltd@gmail.com
: info@geolabengineering.co.ke
Web : www.geolabengineering.co.ke
Cell : 0725643417, 0736 341 339

Head Office & Laboratories
Mina House - Garden Estate
P.O. Box 9514-00100 GPO
Nairobi - Kenya

DENSITY/MOISTURE CONTENT RELATIONSHIP (BS 1377 PART- 4, 3.3 : 1990)

Client name:	**GARMING CONSTRUCTION LIMITED**					
Project/Site name:	**CENTRAL POWER PLANT-NAIVASHA**					
Sampled and submitted by:	GEOLAB	**Date submitted:**	16-Dec-25	**Date tested:**	18-Dec-25	
Sample ID:	A11	**Sample depth (M):**	2.00	**Sample No:**	TS/NAIVASHA/3101	
Moisture addition	50cc	100cc	150cc	200cc	250cc	300cc
Wt of mould + wet material (g)	4440	4509	4573	4607	4595	4574
Wt of mould + Base (g)	3049	3049	3049	3049	3049	3049
Wt wet material (g)	1391	1460	1524	1558	1546	1525
Volume of mould (m^3)	0.903	0.903	0.903	0.903	0.903	0.903
Bulk density (kg/m^3)	**1540**	**1617**	**1687**	**1726**	**1712**	**1689**
Container No	P	DG	V3	DGY	VB	FF
Wt of container + wet material (g)	127.3	162.4	157.0	189.4	192.0	155.1
Wt dry material (g)	116.7	145.9	123.5	132.1	163.3	129.5
Wt of moisture (g)	10.62	16.49	16.56	20.61	28.74	25.64
Wt of container (g)	-	-	-	-	-	-
Moisture content (%)	**9.1**	**11.3**	**13.4**	**15.6**	**17.6**	**19.8**
Dry density (kg/m^3)	**1412**	**1453**	**1488**	**1493**	**1456**	**1410**

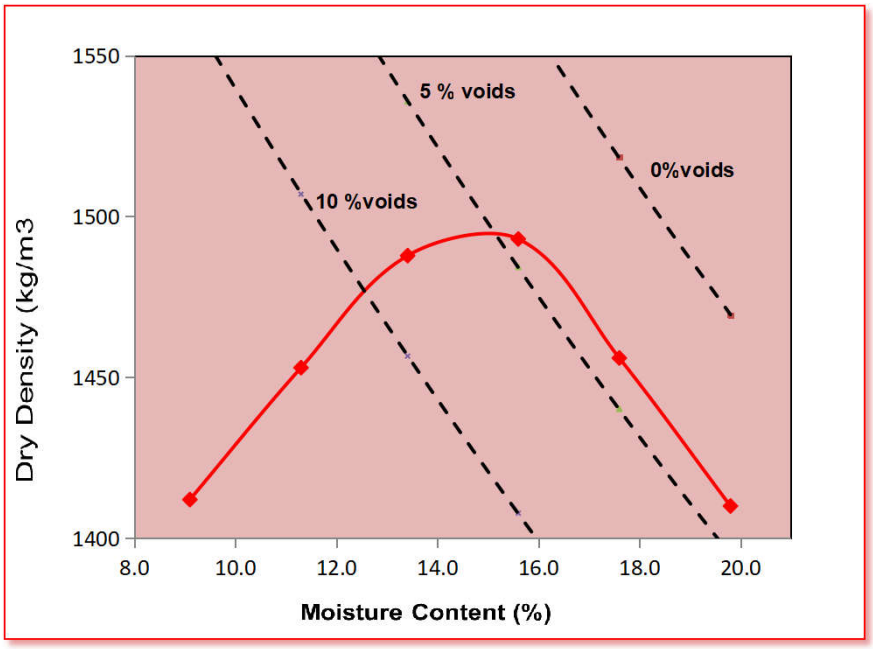

Maximum Dry Density (kg/m^3):	**1495**	**Optimum Moisture Content (%):**	**15.0**
Bulk Density (kg/m^3):	**1719**		


Tested by:	STANLEY	**Date reported:**	18-Dec-25	**Checked by:**	

GEOLAB & ENGINEERING KENYA LIMITED
Independent Materials Testing & Inspection Laboratories
Email : geolabengineeringltd@gmail.com
: info@geolabengineering.co.ke
Web : www.geolabengineering.co.ke
Cell : 0725643417, 0736 341 339

Head Office & Laboratories
Mina House - Garden Estate
P.O. Box 9514-00100 GPO
Nairobi - Kenya

DENSITY/MOISTURE CONTENT RELATIONSHIP (BS 1377 PART- 4, 3.3 : 1990)

Client name:	**GARMING CONSTRUCTION LIMITED**					
Project/Site name:	**CENTRAL POWER PLANT-NAIVASHA**					
Sampled and submitted by:	GEOLAB	**Date submitted:**	16-Dec-25	**Date tested:**	18-Dec-25	
Sample ID:	A11	**Sample depth (M):**	6.00	**Sample No:**	TS/NAIVASHA/3102	
Moisture addition	100cc	150cc	200CC	250cc	300cc	350cc
Wt of mould + wet material (g)	4419	4494	4561	4594	4577	4555
Wt of mould + Base (g)	3049	3049	3049	3049	3049	3049
Wt wet material (g)	1370	1445	1512	1545	1528	1506
Volume of mould (m^3)	0.903	0.903	0.903	0.903	0.903	0.903
Bulk density (kg/m^3)	**1517**	**1601**	**1674**	**1711**	**1692**	**1667**
Container No	SSH	NB	ZS	SE	GF	NN
Wt of container + wet material (g)	136.1	173.2	162.8	179.6	182.8	230.6
Wt dry material (g)	122.6	111.8	118.0	133.8	127.8	130.0
Wt of moisture (g)	13.49	14.76	18.00	23.28	24.92	28.21
Wt of container (g)	-	-	-	-	-	-
Moisture content (%)	**11.0**	**13.2**	**15.3**	**17.4**	**19.5**	**21.7**
Dry density (kg/m^3)	**1367**	**1414**	**1452**	**1457**	**1416**	**1370**

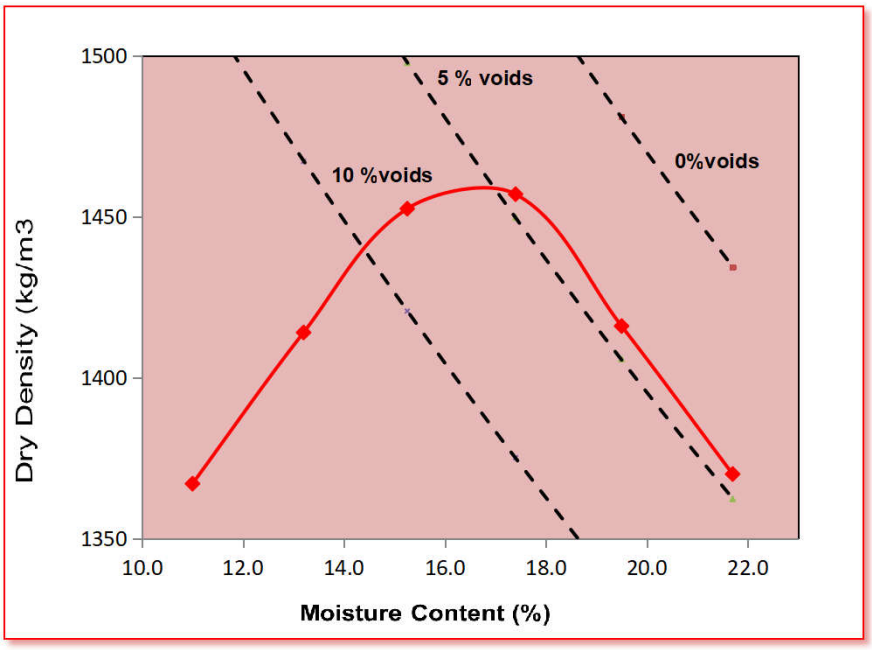

Maximum Dry Density (kg/m^3):	**1460**	**Optimum Moisture Content (%):**	**16.5**
Bulk Density (kg/m^3):	**1701**		


Tested by:	STANLEY	**Date reported:**	18-Dec-25	**Checked by:**	

GEOLAB & ENGINEERING KENYA LIMITED
Independent Materials Testing & Inspection Laboratories
Email : geolabengineeringltd@gmail.com
: info@geolabengineering.co.ke
Web : www.geolabengineering.co.ke
Cell : 0725643417, 0736 341 339

Head Office & Laboratories
Mina House - Garden Estate
P.O. Box 9514-00100 GPO
Nairobi - Kenya

DENSITY/MOISTURE CONTENT RELATIONSHIP (BS 1377 PART- 4, 3.3 : 1990)

Client name:	**GARMING CONSTRUCTION LIMITED**					
Project/Site name:	**CENTRAL POWER PLANT-NAIVASHA**					
Sampled and submitted by:	GEOLAB	**Date submitted:**	16-Dec-25	**Date tested:**	18-Dec-25	
Sample ID:	COMBINED-UNDISTURBED	**Sample depth (M):**	-	**Sample No:**	-	
Moisture addition	300cc	350cc	400CC	450cc	500cc	550cc
Wt of mould + wet material (g)	4465	4540	4601	4635	4620	4599
Wt of mould + Base (g)	3049	3049	3049	3049	3049	3049
Wt wet material (g)	1416	1491	1552	1586	1571	1550
Volume of mould (m^3)	0.903	0.903	0.903	0.903	0.903	0.903
Bulk density (kg/m^3)	**1569**	**1651**	**1718**	**1756**	**1740**	**1716**
Container No	AS	JK	CC	2M	MP	VG
Wt of container + wet material (g)	162.7	173.2	162.8	179.6	182.8	230.6
Wt dry material (g)	145.5	143.2	150.0	122.2	165	166.4
Wt of moisture (g)	17.17	20.05	24.00	22.24	33.50	37.44
Wt of container (g)	-	-	-	-	-	-
Moisture content (%)	**11.8**	**14.0**	**16.0**	**18.2**	**20.3**	**22.5**
Dry density (kg/m^3)	**1403**	**1448**	**1481**	**1486**	**1446**	**1401**

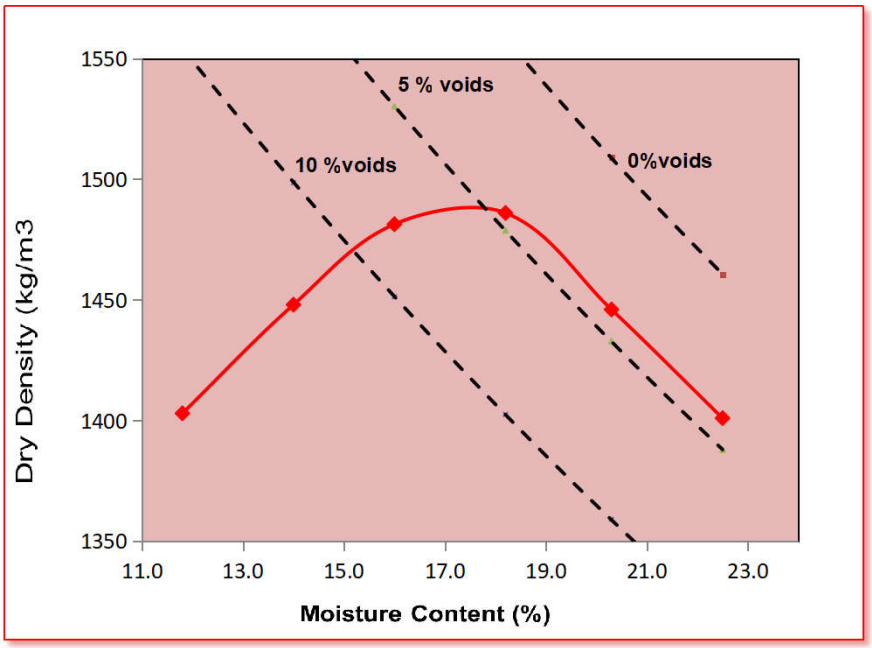

Maximum Dry Density (kg/m^3):	**1489**	**Optimum Moisture Content (%):**	**17.5**
Bulk Density (kg/m^3):	**1750**		


Tested by:	STANLEY	**Date reported:**	18-Dec-25	**Checked by:**	

GEOLAB & ENGINEERING KENYA LIMITED
Independent Materials Testing & Inspection Laboratories
Email : geolabengineeringltd@gmail.com
: info@geolabengineering.co.ke
Web : www.geolabengineering.co.ke
Cell : 0725643417, 0736 341 339

Head Office & Laboratories
Mina House - Garden Estate
P.O. Box 9514-00100 GPO
Nairobi - Kenya

DENSITY/MOISTURE CONTENT RELATIONSHIP (BS 1377 PART- 4, 3.3 : 1990)

Client name:	**GARMING CONSTRUCTION LIMITED**					
Project/Site name:	**CENTRAL POWER PLANT-NAIVASHA**					
Sampled and submitted by:	GEOLAB	**Date submitted:**	16-Dec-25	**Date tested:**	18-Dec-25	
Sample ID:	B11	**Sample depth (M):**	5.00	**Sample No:**	TS/NAIVASHA/3103	
Moisture addition	100cc	150cc	200CC	250cc	300cc	350cc
Wt of mould + wet material (g)	4400	4465	4530	4563	4550	4533
Wt of mould + Base (g)	3049	3049	3049	3049	3049	3049
Wt wet material (g)	1351	1416	1481	1514	1501	1484
Volume of mould (m^3)	0.903	0.903	0.903	0.903	0.903	0.903
Bulk density (kg/m^3)	**1496**	**1568**	**1640**	**1676**	**1663**	**1644**
Container No	DF	R4	EC	GY	AD	DC
Wt of container + wet material (g)	145.3	159.1	157.0	189.4	224.3	188.4
Wt dry material (g)	132.1	141.9	123.5	167.7	189.1	156.2
Wt of moisture (g)	13.21	17.17	17.64	27.67	35.17	32.18
Wt of container (g)	-	-	-	-	-	-
Moisture content (%)	**10.0**	**12.1**	**14.3**	**16.5**	**18.6**	**20.6**
Dry density (kg/m^3)	**1360**	**1399**	**1435**	**1439**	**1402**	**1363**

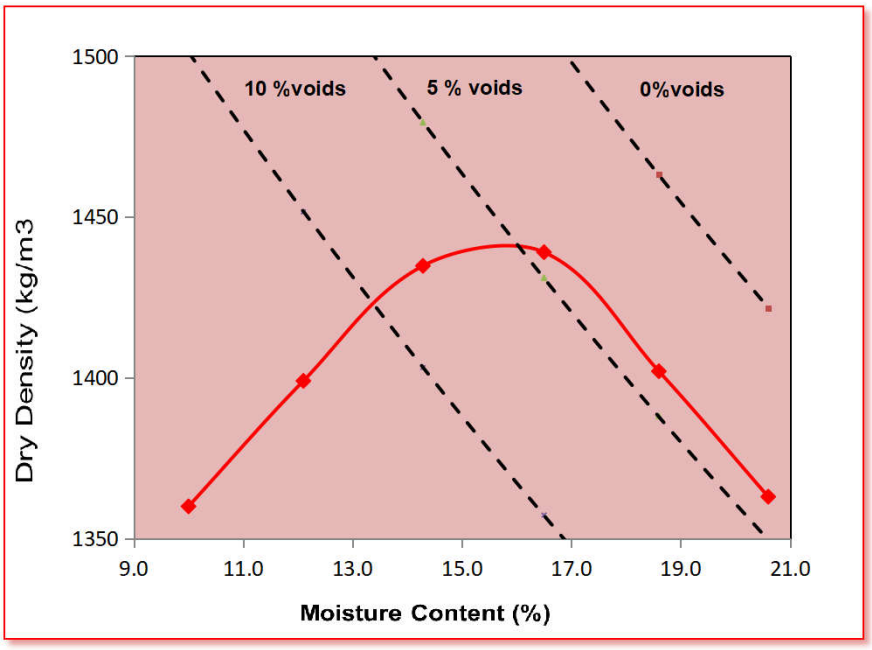

Maximum Dry Density (kg/m^3):	**1441**	**Optimum Moisture Content (%):**	**15.7**
Bulk Density (kg/m^3):	**1667**		


Tested by:	STANLEY	**Date reported:**	18-Dec-25	**Checked by:**	

GEOLAB & ENGINEERING KENYA LIMITED
Independent Materials Testing & Inspection Laboratories
Email : geolabengineeringltd@gmail.com
: info@geolabengineering.co.ke
Web : www.geolabengineering.co.ke
Cell : 0725643417, 0736 341 339

Head Office & Laboratories
Mina House - Garden Estate
P.O. Box 9514-00100 GPO
Nairobi - Kenya

DENSITY/MOISTURE CONTENT RELATIONSHIP (BS 1377 PART- 4, 3.3 : 1990)

Client name:	**GARMING CONSTRUCTION LIMITED**					
Project/Site name:	**CENTRAL POWER PLANT-NAIVASHA**					
Sampled and submitted by:	GEOLAB	**Date submitted:**	16-Dec-25	**Date tested:**	18-Dec-25	
Sample ID:	D11	**Sample depth (M):**	2.00	**Sample No:**	TS/NAIVASHA/3104	
Moisture addition	150cc	200cc	250cc	300cc	350cc	400cc
Wt of mould + wet material (g)	4391	4468	4541	4573	4557	4534
Wt of mould + Base (g)	3049	3049	3049	3049	3049	3049
Wt wet material (g)	1342	1419	1492	1524	1508	1485
Volume of mould (m^3)	0.903	0.903	0.903	0.903	0.903	0.903
Bulk density (kg/m^3)	**1486**	**1571**	**1652**	**1688**	**1670**	**1645**
Container No	CV	DG	J4	MM	WE	DF
Wt of container + wet material (g)	138.0	132.1	157.7	124.0	128.4	190.4
Wt dry material (g)	131.1	122.8	95.5	110.7	112.3	163.6
Wt of moisture (g)	6.95	9.33	9.50	13.28	16.06	26.83
Wt of container (g)	-	-	-	-	-	-
Moisture content (%)	**5.3**	**7.6**	**9.9**	**12.0**	**14.3**	**16.4**
Dry density (kg/m^3)	**1411**	**1460**	**1502**	**1507**	**1461**	**1413**

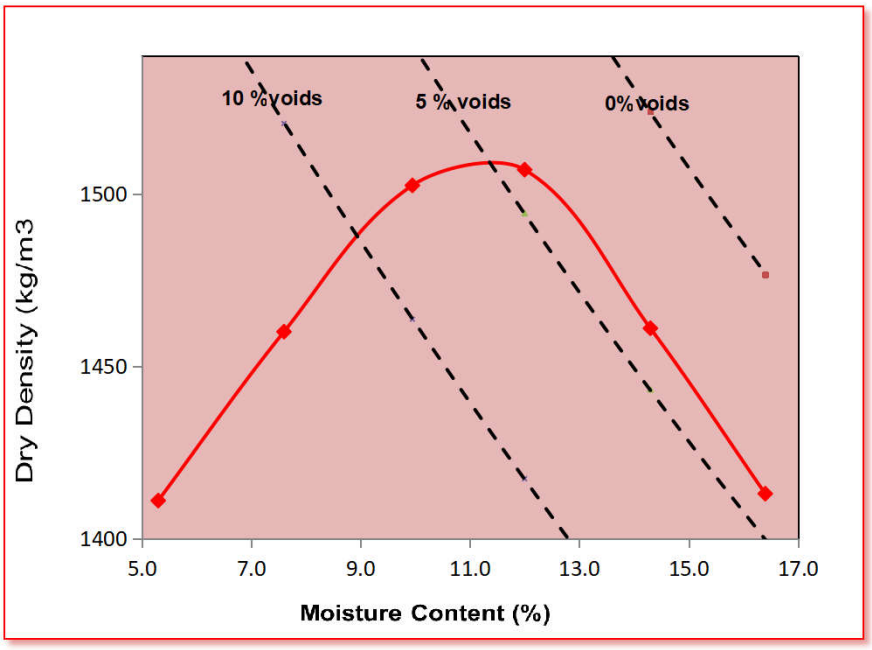

Maximum Dry Density (kg/m^3):	**1510**	**Optimum Moisture Content (%):**	**11.3**
Bulk Density (kg/m^3):	**1681**		


Tested by:	STANLEY	**Date reported:**	18-Dec-25	**Checked by:**	

GEOLAB & ENGINEERING KENYA LIMITED
Independent Materials Testing & Inspection Laboratories
Email : geolabengineeringltd@gmail.com
: info@geolabengineering.co.ke
Web : www.geolabengineering.co.ke
Cell : 0725643417, 0736 341 339

Head Office & Laboratories
Mina House - Garden Estate
P.O. Box 9514-00100 GPO
Nairobi - Kenya

DENSITY/MOISTURE CONTENT RELATIONSHIP (BS 1377 PART- 4, 3.3 : 1990)

Client name:	**GARMING CONSTRUCTION LIMITED**					
Project/Site name:	**CENTRAL POWER PLANT-NAIVASHA**					
Sampled and submitted by:	GEOLAB	**Date submitted:**	16-Dec-25	**Date tested:**	18-Dec-25	
Sample ID:	D11	**Sample depth (M):**	5.00	**Sample No:**	TS/NAIVASHA/3105	
Moisture addition		50cc	100cc	150CC	200cc	250cc	300cc
Wt of mould + wet material (g)		4451	4523	4593	4628	4610	4589
Wt of mould + Base (g)		3049	3049	3049	3049	3049	3049
Wt wet material (g)		1402	1474	1544	1579	1561	1540
Volume of mould (m^3)		0.903	0.903	0.903	0.903	0.903	0.903
Bulk density (kg/m^3)		**1552**	**1632**	**1709**	**1748**	**1729**	**1706**
Container No		BB	VB	GH	BN	CF	CY
Wt of container + wet material (g)		151.3	166.3	162.8	179.6	182.8	230.6
Wt dry material (g)		135.1	145.9	108.5	145.9	145.9	180.6
Wt of moisture (g)		16.21	20.43	17.50	26.70	29.91	41.00
Wt of container (g)		-	-	-	-	-	-
Moisture content (%)		**12.0**	**14.0**	**16.1**	**18.3**	**20.5**	**22.7**
Dry density (kg/m^3)		**1386**	**1432**	**1472**	**1478**	**1435**	**1390**

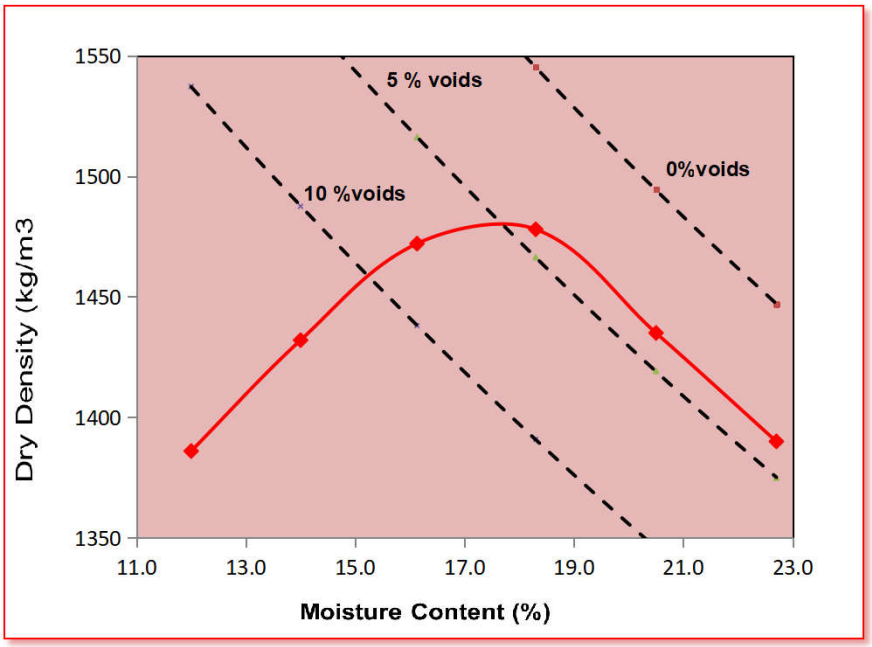

Maximum Dry Density (kg/m^3):	**1480**	**Optimum Moisture Content (%):**	**17.6**
Bulk Density (kg/m^3):	**1740**		

Tested by:	STANLEY	**Date reported:**	18-Dec-25	**Checked by:**	
